


Area Committee

Hendon



Hendon Area Committee
Highways Scheme Update by Ward

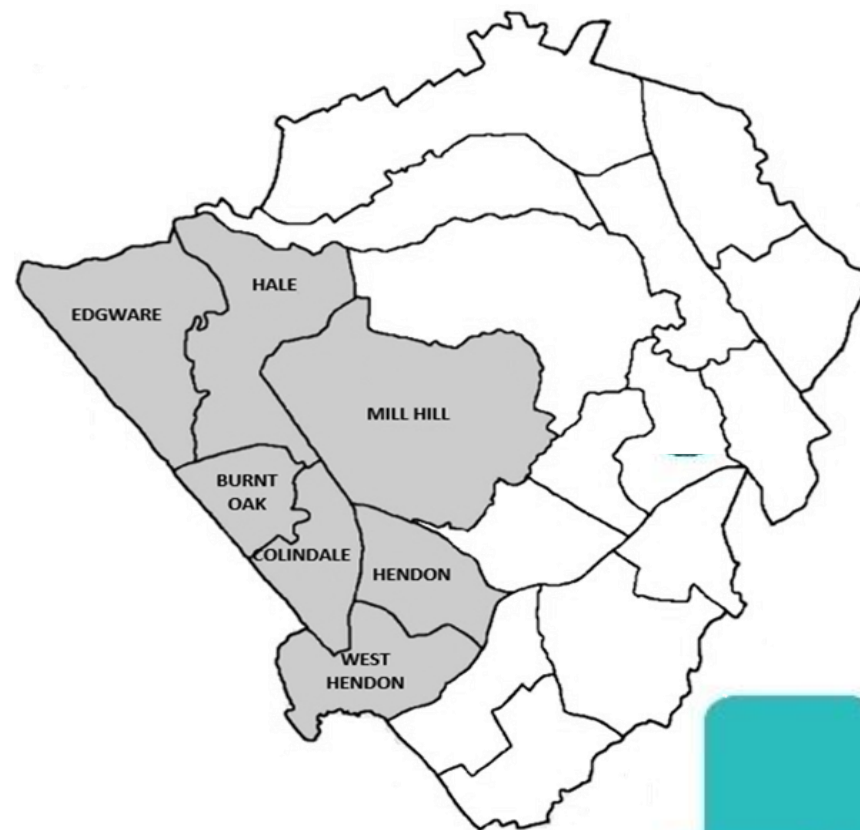



Hendon Highways Schemes - In Progress

Year	Ward	Scheme Name	Scheme Type	Scheme Status	Update
2019/20	Edgware	Hillside Gardens - Speed Survey	Speed Survey	In progress	Report back to March 2020 Hendon Area Committee.
		Parking - Edgwarebury Lane - Implementation	Parking Feasibility	In progress	Design plan to be issued to Ward Councillors in March 2020
		Watling Ave - Loading Bays	Loading Bay	In progress	Site meeting with Ward Councillors to be arranged.
	Hale	Farm Road - Benches	Benches	In progress	Implementation scheduled for March 2020.
		Farm Road & West Way - Signs and Lines	Signs and Markings	In progress	Signage and white lines to be implemented March 2020.
		Farm Road & West Way - Waiting Restrictions	Waiting Restrictions	In progress	Statutory consultation expected March 2020.
		Hale Lane Zebra Crossing - Feasibility	Pedestrian Crossing	In progress	Meeting with Councilors to take place prior to starting Feasibility. Scheuled early March 20
	Hendon	95 Bell Lane - Feasibility Study	Pedestrian Crossing	On hold	Site meeting held with Ward Councillors. Results of the feasibility and recommendation on the location of the crossing report publish but withdrawn from Jan committee. Scheme currently on
	Mill Hill	Limes Ave & Beech Walk NW7 - Ground Stakes	Ground Stakes	In progress	Implementation scheduled March 2020.
		Millway - Implementation	Congestion and Speeding	In progress	Implementation to take place in March 2020. Awaiting date from contractor for VAS sign implementation.
	Mill Hill/ Burnt Oak	Burtonhole - Waiting Restrictions	Waiting Restrictions	In progress	Statutory consultation expected to commence March 2020.
	West Hendon	Brent View Road Waiting Restrictions	Waiting Restrictions	In progress	Chief Officer Decision outlining objections to Statutory Consultation to be finalised February 2020, and implemented March 2020.
		Layfield Crescent - Waiting Restrictions	Waiting Restrictions	In progress	Statutory consultation expected to commence March 2020.
2018/19	Burnt Oak	Barnfield Road/Montrose Avenue – Implementation	Pedestrian Crossing	In progress	Design completed. Road Safety Audit approval required before implementation can begin.
	Edgware	Parking - Goldbeaters Grove	Waiting Restrictions	In progress	Due to parked vehicles the contractor has not completed the works. Officers continue to work with the contractor to get this completed. Expected completion March 2020
	Hale	Parking - Aldridge Avenue	Waiting Restrictions	In progress	Chief Officer Decision outlining objections to Statutory Consultation to be finalised February 2020, and signed-off in March 2020.
	Hendon	Parking - Brent Street - Danescroft	Waiting Restrictions	In progress	Implementation scheduled March 2020
	Mill Hill	Hartley Avenue Ambulance Bay	Ambulance Bay	In progress	Chief Officer Decision outlining objections to Statutory Consultation to be finalised March 2020.
		Lawrence Street / Holcombe Hill - Feasibility Study	Junction Improvement	On hold	Scheme agreed in principle by September 2019 Area Committee. Report deferred subject to funding.





Hendon Highways Schemes - In Progress

Year	Ward	Scheme Name	Scheme Type	Scheme Status	Update
2018/19	Mill Hill	Mill Hill Town Square - Information Boards	Information Boards	In progress	costs exceed value approved by committee. Alternative board to be sourced within budget.
		Parking - Bunns Lane Bridge	Waiting Restrictions	In progress	Implementation of DYL's December 19 linked to Bunn's Lane Junction Improvement Scheme. Statutory Consultation to commence March 2020 for amendment to bay layout in remaining section
		Parking - The Ridgeway (Belmont Farm)	Waiting Restrictions	In progress	Chief Officer Decision outlining objections to Statutory Consultation to be finalised February 2020, and signed-off in March 2020.
	West Hendon	A41/Station Road - Traffic Signal Feasibility	Traffic Signal Feasibility	On hold	Petition being raised at the March 2020 committee which refers to this scheme and also asks for wider and potentially conflicting changes at the junction. Review to be undertaken pending the outcome at committee.
		Parking - Shirehall Lane Parking Bay	Waiting Restrictions	In progress	Objections received. Chief Officer Decision to be finalised and implementation scheduled March 2020.
2017/18	Edgware	Parking - Manor Park Crescent	CPZ - Operational Hours	On hold	Scheme is on hold since the introduction of the nearby Manns Road/Garden City scheme. Discussions to be take place with Councillors to see if there is still a requirement to progress this scheme
	Hendon	Bell Lane / Green Lane - Implementation	Pedestrian Crossing	On hold	Location of Crossing is ongoing. Additional investigation & feasibility study has been undertaken. (linked to 95 Bell Lane Feasibility scheme)
	Mill Hill	Glendor Gardens	Parking Review	In progress	Report back to March 20 Hendon Area Committee (linked to Parking Apex Corner/Watford Way).
		Parking - Daws Lane / Poets Corner	CPZ	In progress	Informal Consultation concluded. Outcome of consultation to be reported back to Hendon Area Committee in June 2020.
2016/17	Colindale	Booth Road, NW9	Traffic & Parking Review	On hold	Scheme put on hold due to the nearby Colindale CPZ scheme. Impact of the Colindale scheme will likely indicate that this scheme is no longer be required. Discussions to progress this scheme, to take place to once Colindale CPZ review is fully complete.
2015/16	Burnt Oak	Footway Parking - Arundal Gardens	Footway Parking	On hold	Scheme originally on hold to until the completion of the 71 footway parking locations that was being undertaken separately but is currently not progressing due to funding. Original allocation of £5,000 is still available and the programming of this scheme will be reviewed in Q1 20/21.
	Mill Hill	Parking Apex Corner/Watford Way	Parking Review	In progress	Funding originally approved in 2015/16 and since been returned. 2018/19 committee agreed that the proposal is be redefined with ward councillors. Proposals to be presented back to March 2020 Hendon Area Committee (Incl. Glendor Gardens).





Hendon Highways Schemes - Completed to Date

Year	Ward	Scheme Name	Scheme Type
2015/16	Burnt Oak	Southbourne Avenue	Footway Parking
	Edgware	Edgwarebury Lane	Pedestrian Refuge
	Hale	Ped Crossing Hale Lane (Implementation)	Pedestrian Crossing
	Mill Hill	Ped Crossing Bunns Lane (Implementation)	Pedestrian Crossing
		Ped Crossing Bunns Lane (Mathilda Marks)	Pedestrian Crossing
		Traffic Abercorn Road	Traffic Scheme
		Traffic Devonshire Road/Pursley Road (Feasibility)	Traffic Calming
		Traffic Devonshire Road/Pursley Road (Implementation)	Traffic Calming
		Traffic Pursley Road/Bunns Lane	Junction Improvement
	West Hendon	Business Bays - Cheyne Walk	Business Bays
		Parking Shirehall Lane	Waiting Restrictions
		Parking Shirehall Lane	Pedestrian Crossing
		Signage West Hendon	Signage

Year	Ward	Scheme Name	Scheme Type
2016/17	Colindale	Colindeep Lane, NW9 - feasibility	Pedestrian Crossing
		Parking Colin Close, NW9	Waiting Restrictions
	Edgware	Parking Garden City - Feasibility	CPZ - Operational Hours
		Parking Green Lane/Oakleigh Gardens	Waiting Restrictions
	Hale	Deansbrook Road, NW7 - YL's	Signage
		Lubavitch of Edgware Kindergarten, 230 Hale Lane	Signs and Keep Clear Marking
		Parking Beechwood Grove / Hale Grove Gardens, NW7	Waiting Restrictions
	Hendon	Pursley Rd/Bunns Lane/Page St - Feasibility	Traffic Scheme
		Bell Lane / Green Lane, NW4 - Feasibility	Pedestrian Crossing
		Brent Green Feasibility (Study Speeding and pedestrian improvements)	Traffic Scheme
		Greyhound Hill - Zebra Crossing - Feasibility	Pedestrian Crossing
		Parking Sydney Grove / Heriot Road, NW4 Feasibility	Waiting Restrictions
	Mill Hill	Langstone Way - Request for a Zebra Crossing	Pedestrian Improvement
		Salcombe Gardens	





Hendon Highways Schemes - Completed to Date

Year	Ward	Scheme Name	Scheme Type
2017/18	Burnt Oak	Barnfield Road/Montrose Avenue – Feasibility	Pedestrian Crossing
		Gaskarth Road - Feasibility	One Way
	Edgware	Broadfields Ave - Feasibility	Pedestrian Crossing
		Parking Garden City - Implementation	CPZ - Operational Hours
		Parking Orchard Drive	Waiting Restrictions
	Hale	Ellesmere Avenue - Feasibility	Traffic Management Scheme
		Westmere Drive – Assess parking capacity	Parking Review
	Hendon	Greyhound Hill - Implementation	Pedestrian Crossing
	Mill Hill	Devonshire Road - Feasibility	Traffic Calming
		Flower Lane Pedestrian Improvements - Feasibility	Pedestrian Improvements
		Langstone Way - Implementation	Pedestrian Improvement

Year	Ward	Scheme Name	Scheme Type
2018/19	Burnt Oak	Watling Ave Alley Gates - Implementation	Gates
		Gaskarth Road – Implementation	One Way
	Colindale	Parking Orchard Gate	Waiting Restrictions
	Edgware	Parking - Edgwarebury Lane - Feasibility	Traffic Flow
	Hale	Westmere Drive Surveys - Speeding & Parking	Surveys
		Ellesmere Avenue - implementation	No Entry
	Mill Hill	Devonshire Road - Implementation	Traffic Calming
		Flower Lane Pedestrian Implementation	Pedestrian Improvements
		Millway - Feasibility Study	Congestion and Speeding
		Parking - Holcombe Hill	Waiting Restrictions
	West Hendon	West Hendon Speeding - Surveys	Surveys

Year	Ward	Scheme Name	Scheme Type
2019/20	Colindale	Colindale Avenue - Keep Clear	Keep Clear
	Hendon	Finchley Lane - Zebra Site Meeting	Zebra Crossing

