


Area Committee

Hendon



Hendon Area Committee
Scheme Update by Ward

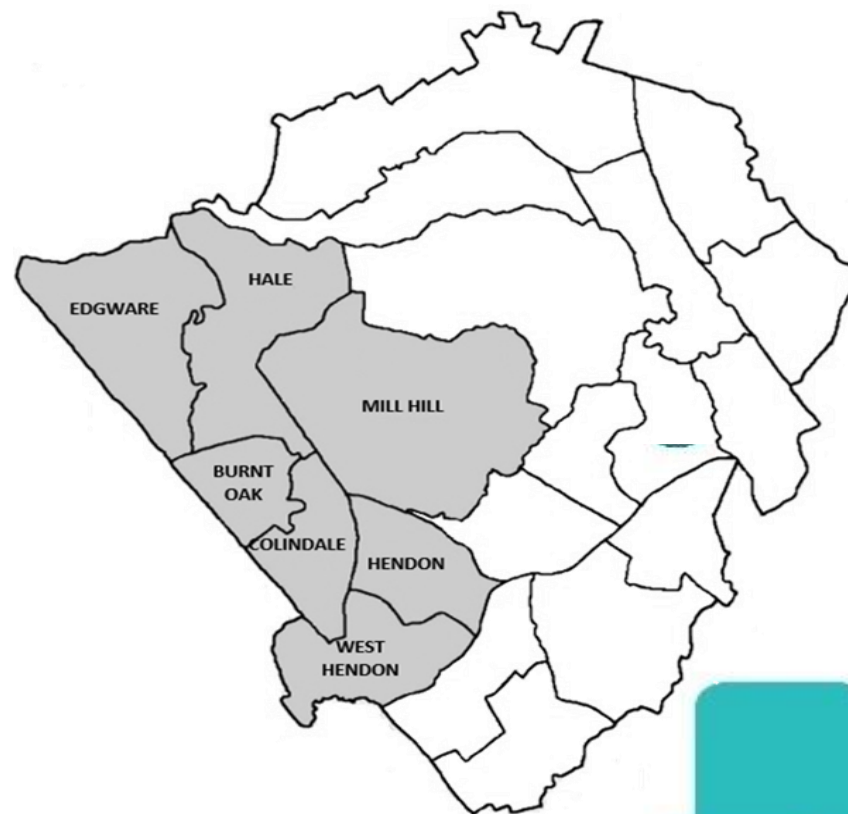



Hendon - Schemes In Progress

Year	Ward	Scheme Name	Scheme Type	Scheme Status	Update
2019/20	Edgware	Hillside Gardens - Speed Survey	Speed Survey	In progress	Report back to Sept 2020 Hendon Area Committee.
		Parking - Edgwarebury Lane - Implementation	Parking Feasibility	In progress	Statutory consultation complete. Chief Officer Decision outlining objections is being finalised for submission in early September 2020.
		Watling Ave - Loading Bays	Loading Bay	In progress	Scheme on hold due to Social Distancing scheme. Currently the kerbside space in Watling Ave is bartered off to widen the pedestrian area for social distancing
	Hale	Farm Road & West Way - Signs and Lines	Signs and Markings	In progress	Scheme delayed due to recent lockdown. Design due to be completed by end of September 2020 with implementation currently planned for October 2020.
		Farm Road & West Way - Waiting Restrictions	Waiting Restrictions	In progress	Statutory consultation complete. Chief Officer Decision outlining objections is being finalised for submission in early September 2020.
	Hendon	95 Bell Lane - Feasibility Study	Pedestrian Crossing	On hold	Site meeting held with Ward Councillors. Results of the feasibility and recommendation on the location of the crossing report publish but withdrawn from Jan committee. Scheme currently on hold, awaiting decision on how to proceed. (linked to Bell Lane/Green Lane Implementation)
	Mill Hill	Millway - Implementation	Congestion and Speeding	In progress	Implementation delayed due to lockdown. Works now due to commence on 21 September 2020.
West Hendon	Layfield Crescent - Waiting Restrictions	Waiting Restrictions	In progress	Statutory consultation complete. Chief Officer Decision outlining objections is being finalised for submission in early September 2020.	
2018/19	Burnt Oak	Barnfield Road/Montrose Avenue – Implementation	Pedestrian Crossing	In progress	Road Safety Audit Complete. Implementation package being prepared and dates to be confirmed with contractor
	Edgware	Parking - Goldbeaters Grove	Waiting Restrictions	In progress	Due to parked vehicles the contractor has not completed the works. Officers continue to work with the contractor to get this completed.
	Hale	Parking - Aldridge Avenue	Waiting Restrictions	In progress	Chief Officer Decision Approved. Due to parked vehicles the contractor has not completed the works. Officers continue to work with the contractor to get this completed.
	Mill Hill	Lawrence Street / Holcombe Hill - Feasibility Study	Junction Improvement	On hold	Scheme agreed in principle by September 2019 Area Committee and deferred to 20/21 subject to funding. This will now be reported back to September 2020 Committee.
		Mill Hill Town Square - Information Boards	Information Boards	In progress	Delayed due to lockdown. New quotes have been requested but it's likely that it will still be more than the allocated budget. Once received, it will be brought to the Mill Hill forum to discuss options.
		Parking - The Ridgeway (Belmont Farm)	Waiting Restrictions	In progress	Due to parked vehicles the contractor has not completed the works. Officers continue to work with the contractor to get this completed.
	West Hendon	A41/Station Road - Traffic Signal Feasibility	Traffic Signal Feasibility	On hold	Drawings and scheme details have been produced for TfL, to allow them to carry out the signals design and estimate for this work.





Hendon - Schemes In Progress

Year	Ward	Scheme Name	Scheme Type	Scheme Status	Update
2017/18	Edgware	Parking - Manor Park Crescent	CPZ - Operational Hours	On hold	Scheme is on hold since the introduction of the nearby Manns Road/Garden City scheme. Discussions to be take place with Councillors to see if there is still a requirement to progress this scheme
	Hendon	Bell Lane / Green Lane - Implementation	Pedestrian Crossing	On hold	Location of Crossing is ongoing. Additional investigation & feasibility study has been undertaken. (linked to 95 Bell Lane Feasibility scheme)
	Mill Hill	Glendor Gardens	Parking Review	In progress	Report back to September 2020 Hendon Area Committee (see Parking Apex Corner/Watford Way below).
Parking - Daws Lane / Poets Corner		CPZ	In progress	Informal Consultation concluded. Outcome of consultation to be reported back to Hendon Area Committee in September 2020.	
2016/17	Colindale	Booth Road, NW9	Traffic & Parking Review	On hold	Scheme to be formally closed as covered by the Colindale CPZ scheme
2015/16	Burnt Oak	Footway Parking - Arundal Gardens	Footway Parking	On hold	Scheme originally on hold to until the completion of the 71 footway parking locations that were being undertaken separately, but is no longer progressing due to funding. The original allocation of £5,000 is still available and will be reviewed for programming in Q3.
	Mill Hill	Parking Apex Corner/Watford Way	Parking Review	In progress	Funding originally approved in 2015/16 and since been returned. 2018/19 committee agreed that the proposal is be redefined with ward councillors. Proposals to be presented back to September 2020 Hendon Area Committee (Incl. Glendor Gardens).





Hendon Schemes - Completed

Year	Ward	Scheme Name	Scheme Type	
2015/16	Burnt Oak	Southbourne Avenue	Footway Parking	
	Edgware	Edgwarebury Lane	Pedestrian Refuge	
	Hale	Ped Crossing Hale Lane (Implementation)	Pedestrian Crossing	
	Mill Hill		Ped Crossing Bunns Lane (Implementation)	Pedestrian Crossing
			Ped Crossing Bunns Lane (Mathilda Marks)	Pedestrian Crossing
			Traffic Abercorn Road	Traffic Scheme
			Traffic Devonshire Road/Pursley Road (Feasibility)	Traffic Calming
			Traffic Devonshire Road/Pursley Road (Implementation)	Traffic Calming
	West Hendon		Traffic Pursley Road/Bunns Lane	Junction Improvement
			Business Bays - Cheyne Walk	Business Bays
			Parking Shirehall Lane	Waiting Restrictions
			Parking Shirehall Lane	Pedestrian Crossing
			Signage West Hendon	Signage

Year	Ward	Scheme Name	Scheme Type	
2016/17	Colindale	Colindeep Lane, NW9 - feasibility	Pedestrian Crossing	
		Parking Colin Close, NW9	Waiting Restrictions	
	Edgware	Parking Garden City - Feasibility	CPZ - Operational Hours	
		Parking Green Lane/Oakleigh Gardens	Waiting Restrictions	
	Hale	Deansbrook Road, NW7 - YL's	Signage	
		Lubavitch of Edgware Kindergarten, 230 Hale Lane	Signs and Keep Clear Marking	
		Parking Beechwood Grove / Hale Grove Gardens, NW7	Waiting Restrictions	
	Hendon		Pursley Rd/Bunns Lane/Page St - Feasibility	Traffic Scheme
			Bell Lane / Green Lane, NW4 - Feasibility	Pedestrian Crossing
			Brent Green Feasibility (Study Speeding and pedestrian improvements)	Traffic Scheme
			Greyhound Hill - Zebra Crossing - Feasibility	Pedestrian Crossing
			Parking Sydney Grove / Heriot Road, NW4 Feasibility	Waiting Restrictions
	Mill Hill		Langstone Way - Request for a Zebra Crossing	Pedestrian Improvement
			Salcombe Gardens	





Hendon Schemes - Completed

Year	Ward	Scheme Name	Scheme Type
2017/18	Burnt Oak	Barnfield Road/Montrose Avenue – Feasibility	Pedestrian Crossing
		Gaskarth Road - Feasibility	One Way
	Edgware	Broadfields Ave - Feasibility	Pedestrian Crossing
		Parking Garden City - Implementation	CPZ - Operational Hours
		Parking Orchard Drive	Waiting Restrictions
	Hale	Ellesmere Avenue - Feasibility	Traffic Management Scheme
		Westmere Drive – Assess parking capacity	Parking Review
	Hendon	Greyhound Hill - Implementation	Pedestrian Crossing
	Mill Hill	Devonshire Road - Feasibility	Traffic Calming
		Flower Lane Pedestrian Improvements - Feasibility	Pedestrian Improvements
Langstone Way - Implementation		Pedestrian Improvement	

Year	Ward	Scheme Name	Scheme Type
2019/20	Colindale	Colindale Avenue - Keep Clear	Keep Clear
	Hale	Farm Road - Benches	Benches
	Hendon	Finchley Lane - Zebra Site Meeting	Zebra Crossing
	Mill Hill/ Burnt Oak	Burtonhole - Waiting Restrictions	Waiting Restrictions
	Mill Hill	Limes Ave & Beech Walk NW7 - Ground Stakes	Ground Stakes
	West Hendon	Brent View Road Waiting Restrictions	Waiting Restrictions

Year	Ward	Scheme Name	Scheme Type
2018/19	Burnt Oak	Watling Ave Alley Gates - Implementation	Gates
		Gaskarth Road – Implementation	One Way
	Colindale	Parking Orchard Gate	Waiting Restrictions
	Edgware	Parking - Edgwarebury Lane - Feasibility	Traffic Flow
	Hale	Westmere Drive Surveys - Speeding & Parking	Surveys
		Ellesmere Avenue - implementation	No Entry
	Hendon	Parking - Brent Street Danescroft	Waiting Restrictions
	Mill Hill	Devonshire Road - Implementation	Traffic Calming
		Flower Lane Pedestrian Implementation	Pedestrian Improvements
		Millway - Feasibility Study	Congestion and Speeding
		Parking - Holcombe Hill	Waiting Restrictions
		Bunns Lane Bridge	Waiting Restrictions
		Hartley Avenue Ambulance Bay	Ambulance Bay
	West Hendon	West Hendon Speeding - Surveys	Surveys
Parking - Shirehall Lane Parking Bay		Waiting Restrictions	

